


Appendix 11 - Detailed project plan



ID	Task Name	Duration	Start	Finish	Predecessor	Resource Names	Qtr 1, 2011	Qtr 2, 2011	Qtr 3, 2011	Qtr 4, 2011	Qtr 1, 2012	Qtr 2, 2012	Qtr 3, 2012	Qtr 4, 2012	Qtr 1, 2013	Qtr 2, 2013	Qtr 3, 2013	Qtr 4, 2013	Qtr 1, 2014	Qtr 2, 2014	Qtr 3, 2014	Qtr 4, 2014	Qtr 1, 2015	Qtr 2, 2015	Qtr 3, 2015	Qtr 4, 2015	Qtr 1, 2016	Qtr 2, 2016	Qtr 3, 2016	Qtr 4, 2016	
286	Stage 4 Final Concept	60 days	Mon 07/09/15	Fri 27/11/15	284	Sustrans																									
287	Construction	90 days	Mon 30/11/15	Fri 01/04/16	286	NCC Highways																									
288	Practical Completion	0 days	Fri 01/04/16	Fri 01/04/16	287																										
289	City Centre Cycle Hub	750 days	Fri 01/03/13	Thu 14/01/16																											
290	Feasibility	60 days	Fri 01/03/13	Thu 23/05/13		Sustrans																									
291	incorporation	7 days	Fri 24/05/13	Mon 03/06/13	290	Sustrans																									
292	secure premises	0 days	Thu 23/05/13	Thu 23/05/13	290	Sustrans																									
293	Fitout & Recruitment	90 days	Fri 24/05/13	Thu 26/09/13	292	Sustrans																									
294	Opening	0 days	Thu 26/09/13	Thu 26/09/13	293	Sustrans																									
295	Promotion & Operation	600 days	Fri 27/09/13	Thu 14/01/16	294	Sustrans																									

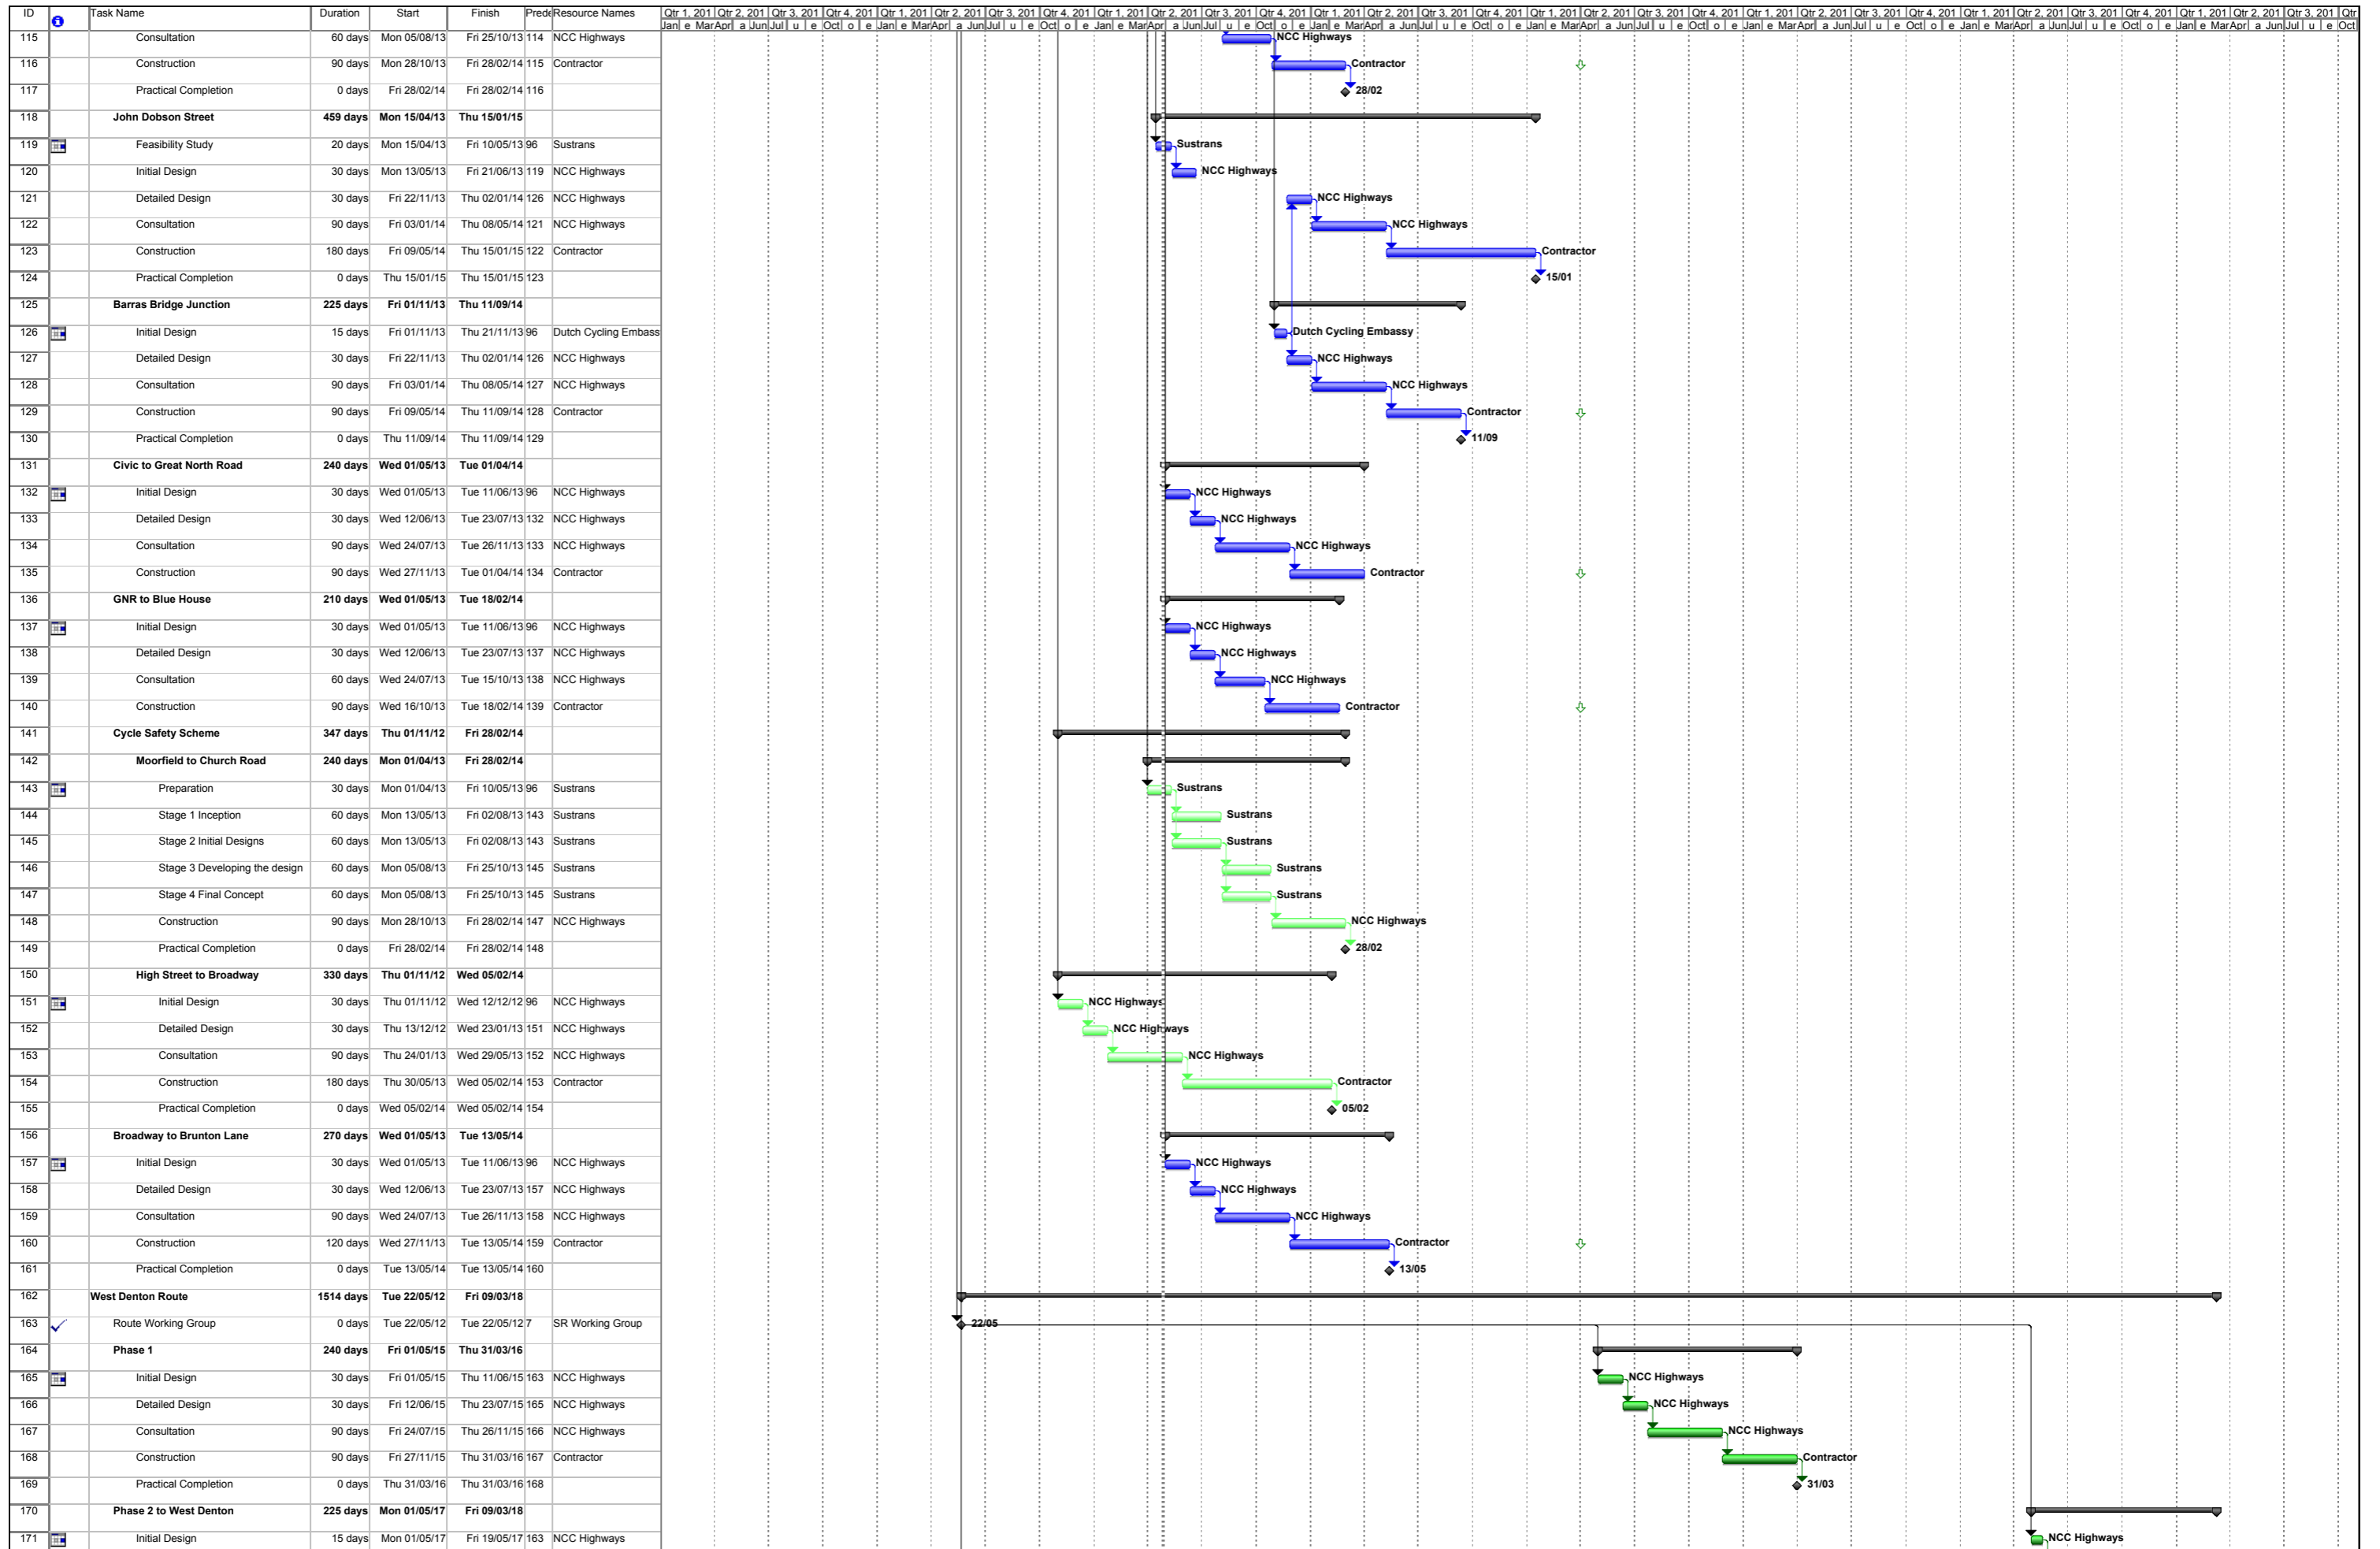
